

I-5 Widening Project Orange County Line to I-605

Status Report


February 1, 2006

Doug Failing

Caltrans, District 7 Director



I-5 Santa Ana Freeway Corridor

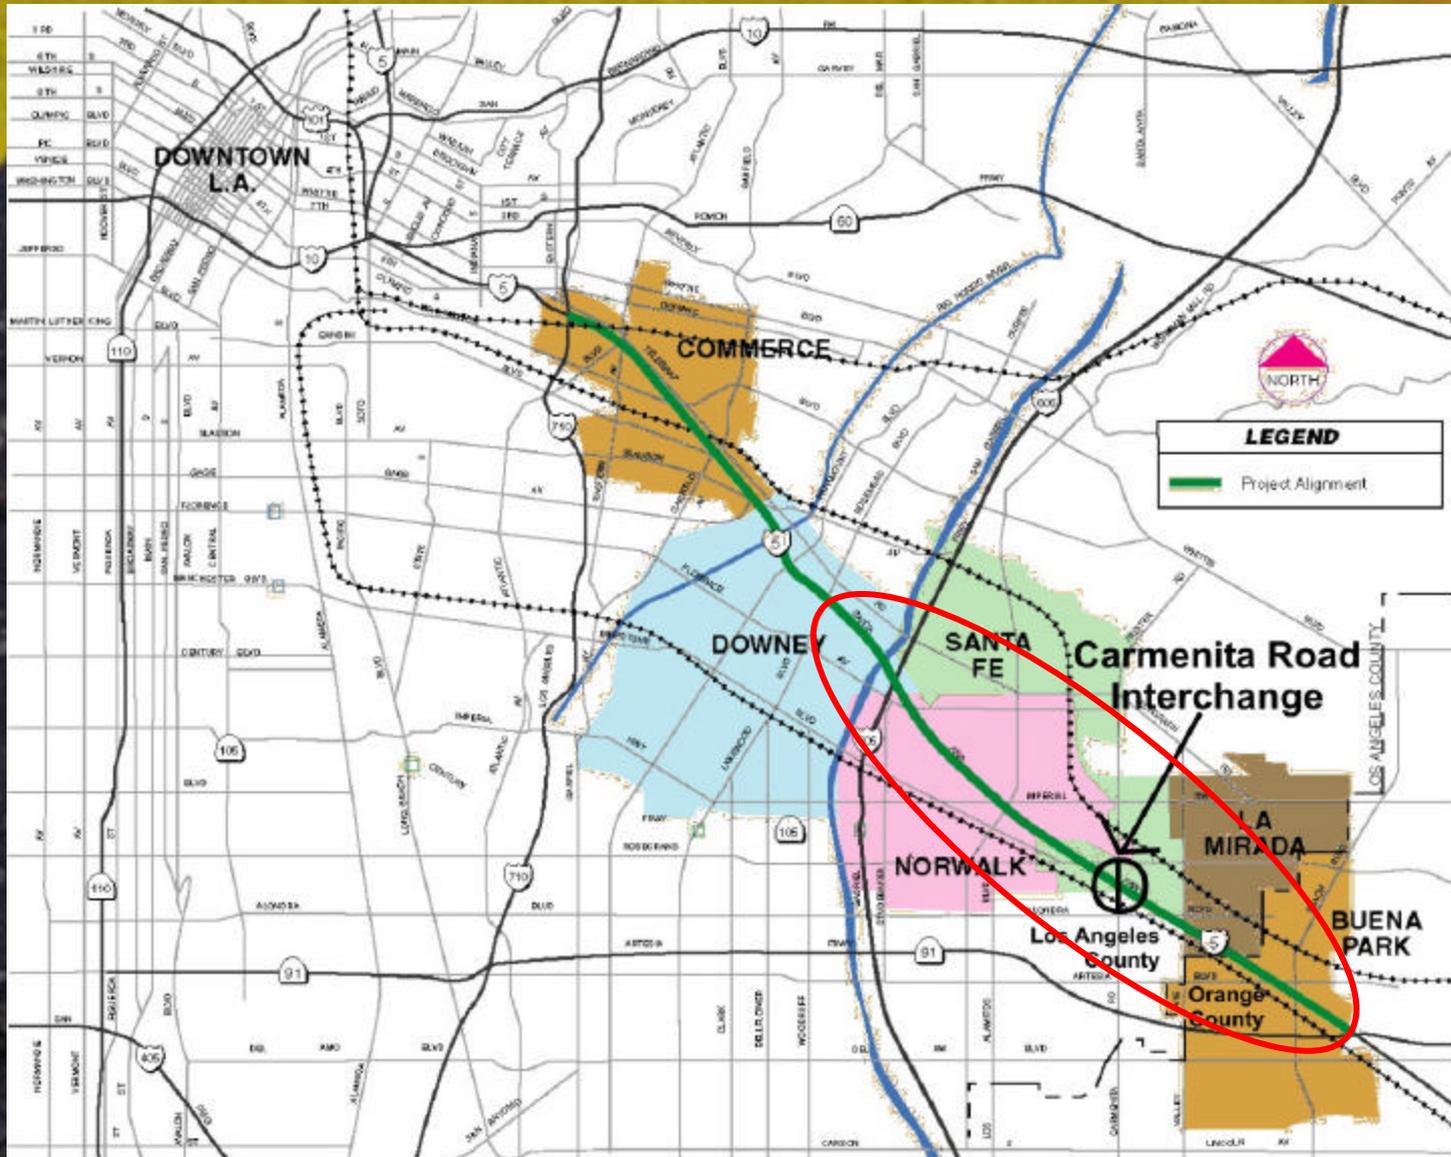

Current Schedule

Project Report & Environmental Document	December 2006
Complete Design	January 2009
Begin Construction	January 2010
End Construction	December 2015

Current Project Status

- **Executed the Performance Agreement and the Supplemental MOU**
- **Established Steering Committee**
- **Landscape and Aesthetics Subcommittee**
 - The Aesthetics Master Plan is targeted to be completed this summer for the entire freeway
- **Revising design to reduce R/W impacts**
 - Developing a 12 lane alternative that avoids expensive properties such as car dealerships
 - Implementing viable Value Analysis recommendations

Current Project Status (Cont'd)

- **Exploring methods to maximize remnant property's redevelopment value**
- **Draft EIR planned to be circulated this spring**
 - **Will be holding several outreach meetings with community, to discuss the Project's scope.**

Status of adjacent projects

Carmenita Interchange

- **Completed Geometric Plans**
- **Executed Freeway Agreements**
- **Started the Right of Way process**
- **Caltrans, Metro and JPA continue to work together to reduce right of way cost**

Status of adjacent projects I-605 to I-710

- **Received funding for the Environmental Document**
- **Environmental process will mobilize starting July 2006**

