


# Hopland ADA Project Schedule

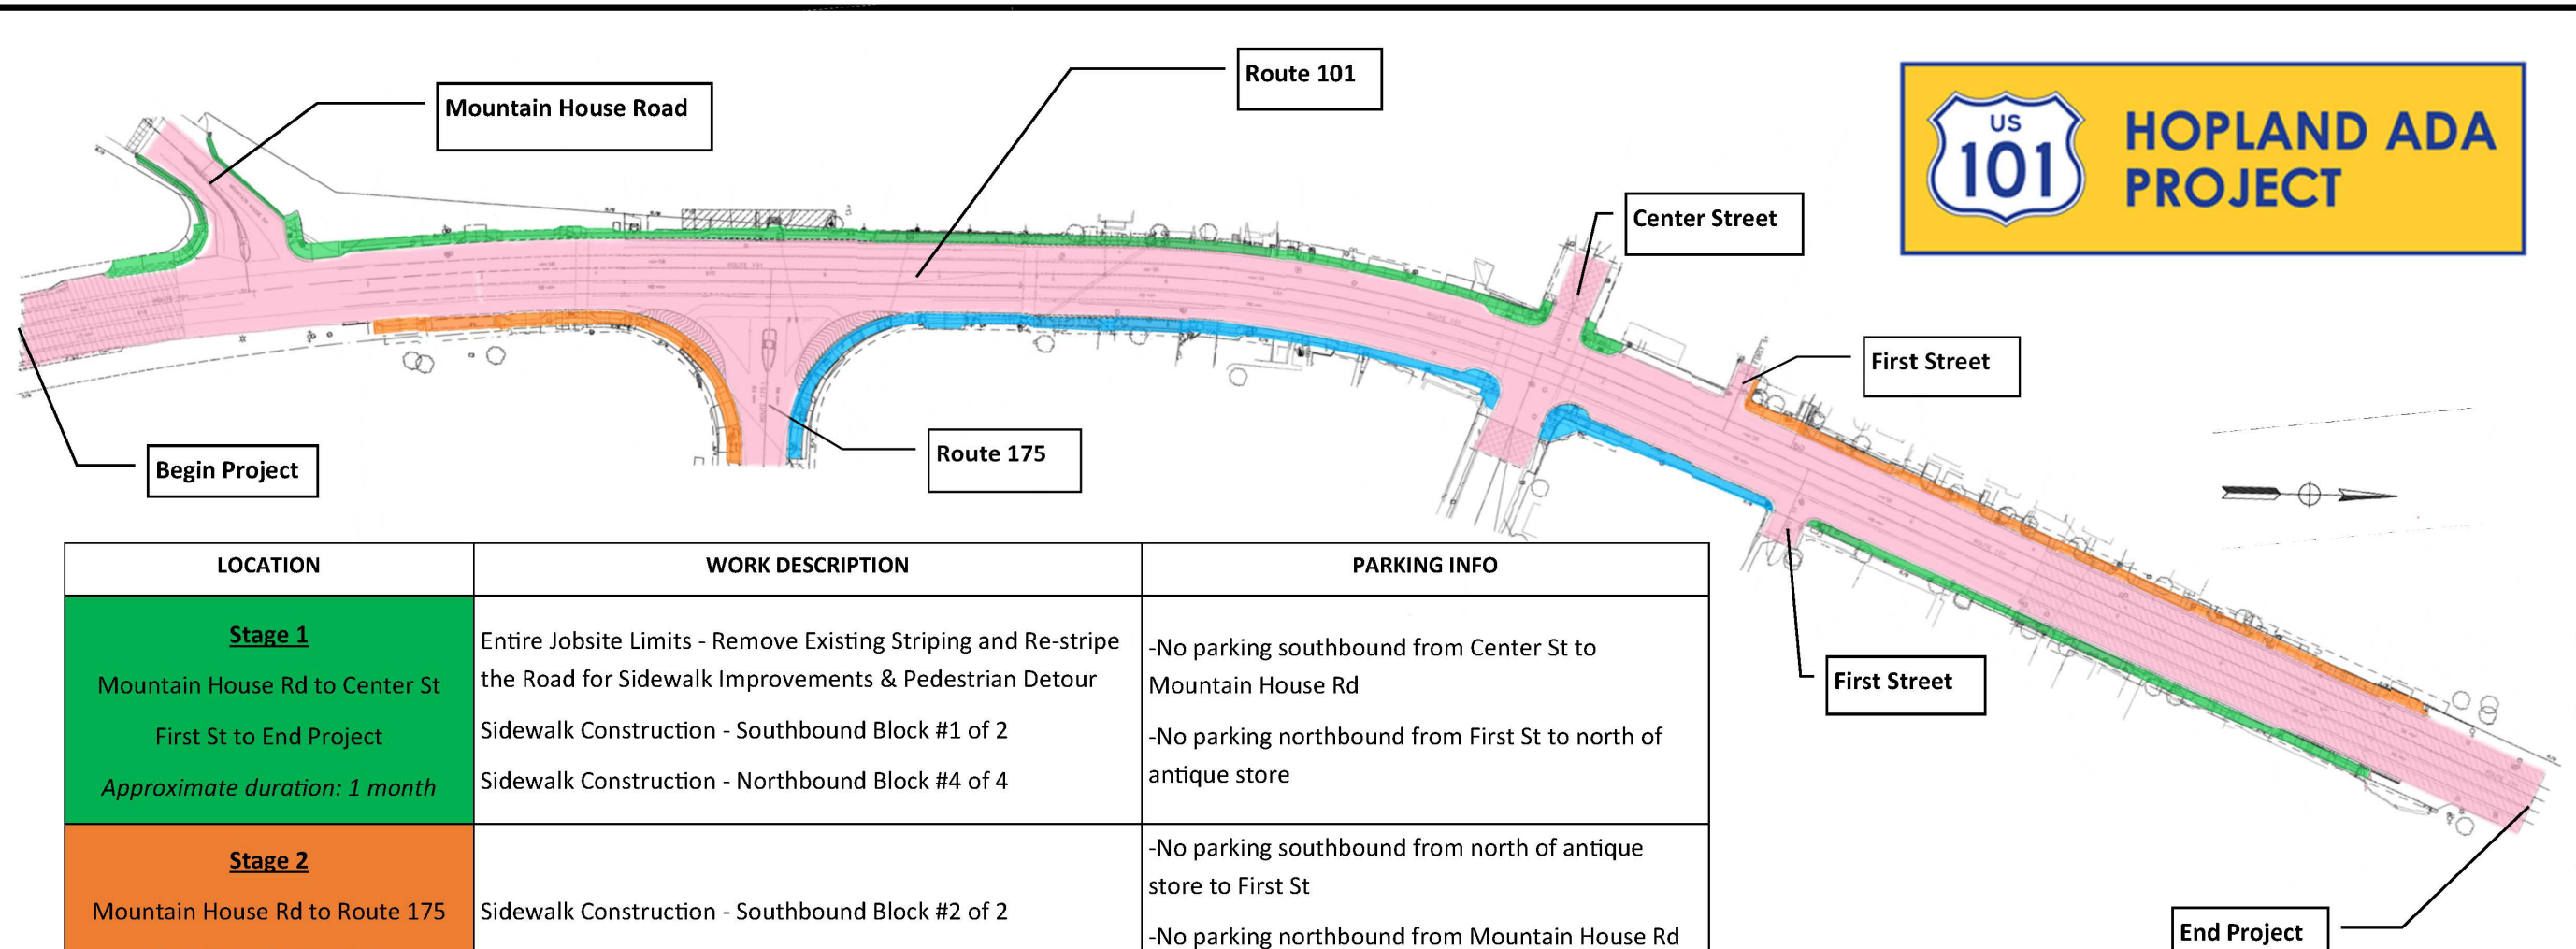

LOCATION	WORK DESCRIPTION	PARKING INFO
<b>Stage 1</b> Mountain House Rd to Center St First St to End Project <i>Approximate duration: 1 month</i>	Entire Jobsite Limits - Remove Existing Striping and Re-stripe the Road for Sidewalk Improvements & Pedestrian Detour Sidewalk Construction - Southbound Block #1 of 2 Sidewalk Construction - Northbound Block #4 of 4	-No parking southbound from Center St to Mountain House Rd -No parking northbound from First St to north of antique store
<b>Stage 2</b> Mountain House Rd to Route 175 First St to End Project <i>Approximate duration: 1 month</i>	Sidewalk Construction - Southbound Block #2 of 2 Sidewalk Construction - Northbound Block #1 of 4	-No parking southbound from north of antique store to First St -No parking northbound from Mountain House Rd to Route 175
<b>Stage 3</b> Route 175 to Center St Center St to First St <i>Approximate duration: 1 month</i>	Sidewalk Construction - Northbound Block #2 of 4 Sidewalk Construction - Northbound Block #3 of 4	-No parking northbound from Route 175 to First St
<b>Stage 4</b> Entire Project Limits <i>Approximate duration: 4 months</i>	Roadway Excavation Fine Grade Roadway Lean Concrete Base Raise Utilities Hot Mix Asphalt Paving	-Parking restricted throughout project limits
<b>Stage 5</b> Entire Project Limits <i>Approximate duration: 1 month</i>	Striping & Signage Project Complete	-No parking restrictions

For More Information:

<https://dot.ca.gov/caltrans-near-me/district-1/d1-projects/d1-hopland-ada>
