

BRIDGE SEISMIC RETROFIT PROJECT PROGRESS REPORT



DEPARTMENT OF WATER RESOURCES

DIVISION OF OPERATIONS AND MAINTENANCE

Teresa Sutliff, Chief
Civil Engineering Branch


CTC MEETING - February 2006

Background

- 24 bridges were identified by Caltrans to be potentially seismically deficient
- 9 bridges are owned by Department of Water Resources (DWR) and 15 bridges are owned by US Bureau of Reclamation (USBR)
- DWR signed an MOU with Caltrans in January 2005
- DWR secured funding for Preliminary Engineering (PE) for State Fiscal Year 05-06



STATE WATER PROJECT FIELD DIVISION INDEX

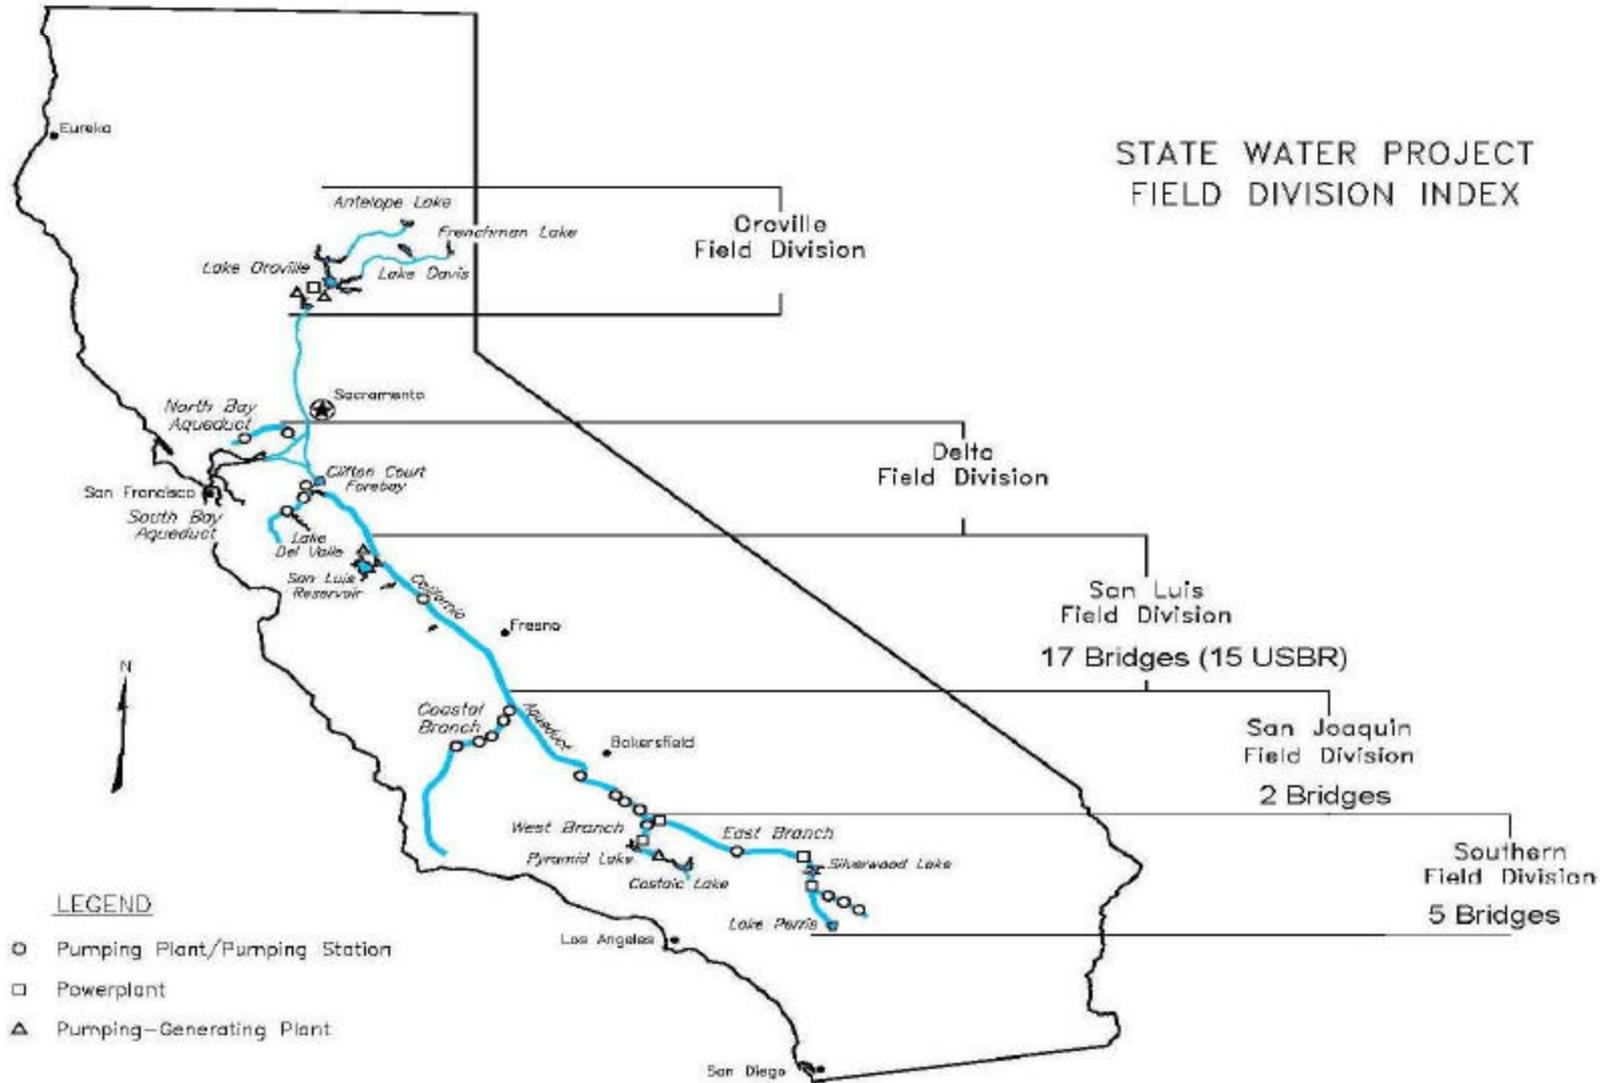

Progress Report

- Caltrans District 6 is DWR's main contact for all 24 bridges
- Caltrans approved the Authorization to Proceed for PE on 8/27/05 for 2 projects: one for 9 DWR bridges and one for 15 USBR bridges



Progress Report (cont.)

- USBR will analyze 15 bridges
- DWR will analyze 9 bridges
- Program Supplement Agreement (PSA) for DWR bridges was signed in January 2006
- DWR still needs USBR approval for PSA
- DWR is working with USBR on a Letter Agreement for analysis of 15 bridges



Project Schedule

DWR Bridges

- Analysis of 9 bridges is 34% complete and is expected to be 100% complete by July 2006
- Design is planned to start in October 2006
- Construction is planned to start in April 2008 and longer, if necessary.



Project Schedule (cont.)

USBR Bridges

- USBR will begin analysis once Letter of Agreement with DWR is signed, anticipate in March 2006
- USBR will complete the analysis in 8 months
- Design is planned to start in April 2007





QUESTIONS
