

State of California
Business, Transportation and Housing Agency
Department of Transportation

Prepared By:
Jim Nicholas
Program Manager,
Transportation Programming
(916) 654-4013

Proposed

PROGRAM AMENDMENTS
STIP Amendment 00S-019
Notice Item
CTC Meeting: March 28-29, 2001

Agenda Item: 2.1b.(6)

Original Signed By

W. J. EVANS, Deputy Director
Finance
March 1, 2001

STIP AMENDMENT 00S-019 NOTICE

SUMMARY

This amendment delays \$5,485,000 in Regional Improvement Program (RIP) funds from FY 2001-02 to FY 2003-04 for the construction components on an auxiliary lane project on Route 5 in San Diego County. There is no change in the total funding for the project.

RECOMMENDATION

The San Diego Association of Governments (SANDAG) and the Department are requesting this amendment.

RESOLUTION

Resolved, that the California Transportation Commission (CTC) revise the 2000 State Transportation Improvement Program (STIP) at the end of the 30-day notice period as follows:

Revises:

Project Information								
County:	CT District:	PPNO:	EA:	Element:	Const Year:	PM Back	PM Ahead	Route/Corridor
San Diego	11	0135G	065101 065100	CTCO	2001-02 2003-04	R34.8	R35.7	5
Project Title:	Del Mar Heights Auxiliary Lane							
Sponsor:	Caltrans							
Implementing Agency:	Caltrans							
RTPA/CTC:	San Diego Association of Governments							
Location:	In San Diego County in San Diego from 1.1 Kilometers north of Del Mar Heights Road Overcrossing to 1.0 Kilometers south of via de la Valle Overcrossing							
Description:	Construction of Auxiliary Lane Northbound							

STIP Programming - RIP							
(Dollars in Thousands)							
Component	PRIOR	2000/2001	2001/2002	2002/2003	2003/2004		Total
PA&ED	\$126						\$126
PS&E	\$410						\$410
R/W SUP		\$26					\$26
CON SUP			\$635		\$635		\$635
R/W		\$53					\$53
CON			\$4,850		\$4,850		\$4,850
TOTAL	\$536	\$79	\$5,485		\$5,485		\$6,100

March 28-29, 2001

BACKGROUND


This amendment delays \$5,485,000 in Regional Improvement Program (RIP) funds from FY 2001-02 to FY 2003-04 for the construction components on an auxiliary lane project on Route 5 in San Diego County.

During the preliminary environmental review phase, three endangered species were found in the area (California gnatcatchers, Pacific pocket mouse and the Light-footed clapper rail). It is estimated an additional 18 months are needed to complete the environmental review process to satisfy the requirements of the United States Fish and Wildlife Service and the California Department of Fish and Game. This will delay the construction components until fiscal year 2003-04.

ATTACHMENT

STIP AMENDMENT 00S-019

Location Map

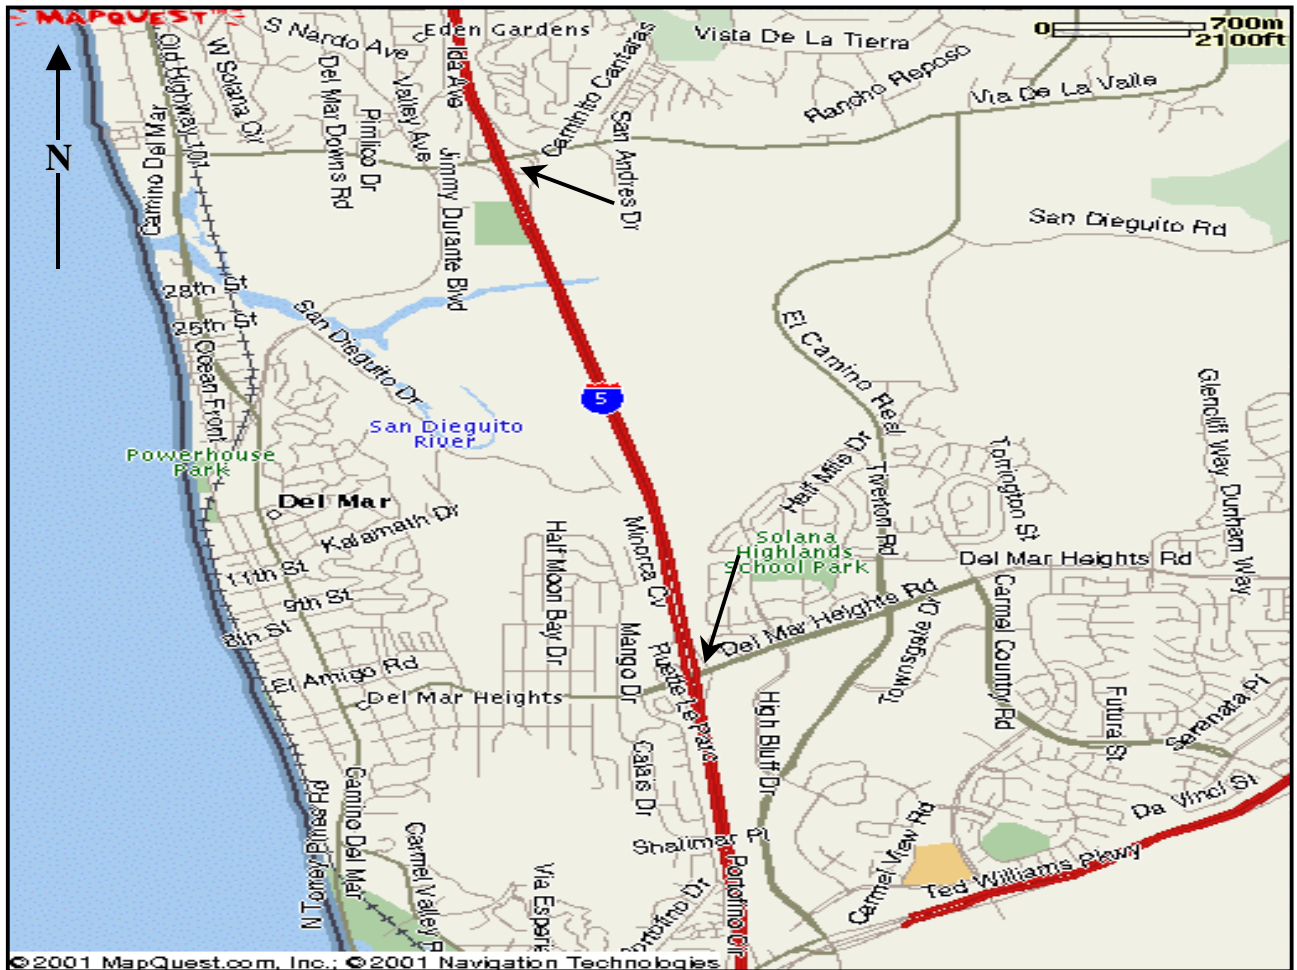

11-San Diego
PPNO 0135G

Location: In San Diego, north of Del Mar Heights Road
Overcrossing to Via de La Valle Overcrossing

Description: Construct northbound auxiliary lane

