


**Table 5-4.1 Request for Information and Potential Claim Process**

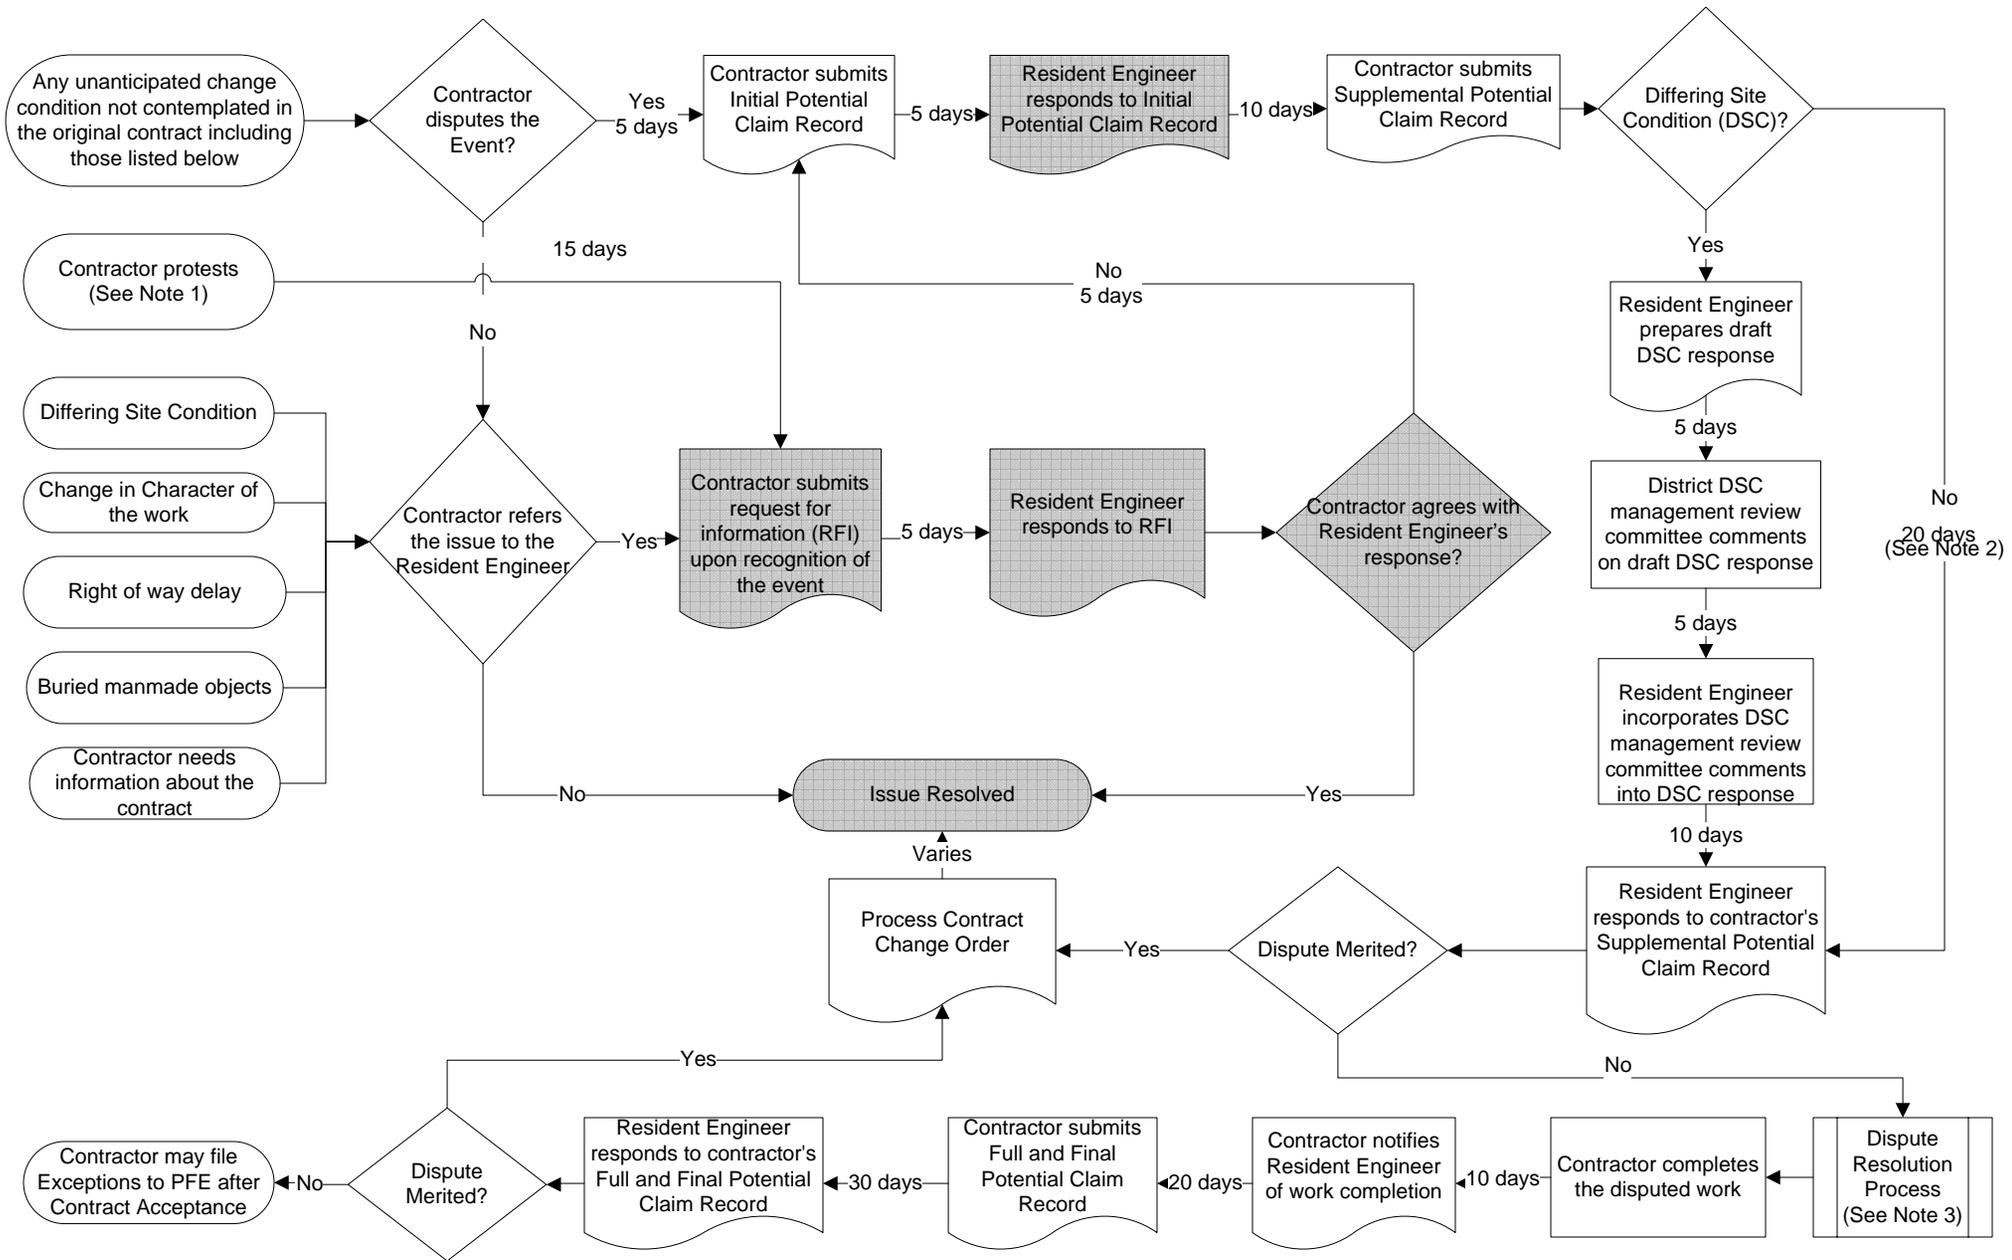

Note 1 - Contractor may protest an approved CCO not executed by the contractor, compensation for work specified in the CCO, adjustment of contract time, weekly statement of working days, progress payment, delays, liquidated damages, and any decision by the Resident Engineer.

Note 2- The Resident Engineer should respond to the supplemental potential claim record as quickly as possible not to exceed 20 days.

Note 3- The Contractor must exhaust the dispute resolution provisions by referring the potential claim to the dispute resolution advisor or dispute resolution board when required
